

Seguimiento de las Fuentes - X +

mt.hacienda.gob.mx/mt-web/programa/Costra/avances.dtl?proyecto=1513347

| Periodo        | Recaudado    | Comprometido | Devengado    | Ejercido     | Pagado       | Avance    | Acción       |
|----------------|--------------|--------------|--------------|--------------|--------------|-----------|--------------|
| 2019 / ABR-JUN | \$250,000.00 | \$250,000.00 | \$250,000.00 | \$126,812.00 | \$126,812.00 | 50.72%    | ✓ Confirmado |
| 2019 / JUL-SEP | \$250,000.00 | \$250,000.00 | \$250,000.00 | \$214,852.27 | \$214,852.27 | 85.94091% | ✎ Editar     |
| 2019 / ENE-MAR | \$0.00       | \$0.00       | \$0.00       | \$0.00       | \$0.00       | 0%        | ✓ Confirmado |

Avances Físicos


Promedio del Porcentaje de Avances Físicos **85.94 %**

Unidad de Medida: Kilómetros lineal    Meta: 11.6    Meta Modificada: 11.6    [Registrar Avance](#)


Porcentaje Total de la Meta **85.94%**

| Periodo      | Avance      | Porcentaje | Acción       |
|--------------|-------------|------------|--------------|
| 2019 JUL-SEP | 9.969145328 | 85.94%     | ✎ Editar     |
| 2019 ABR-JUN | 0.00        | 50.69%     | ✓ Confirmado |
| 2019 ENE-MAR | 0           | 0.00%      | ✓ Confirmado |

Las Canoas

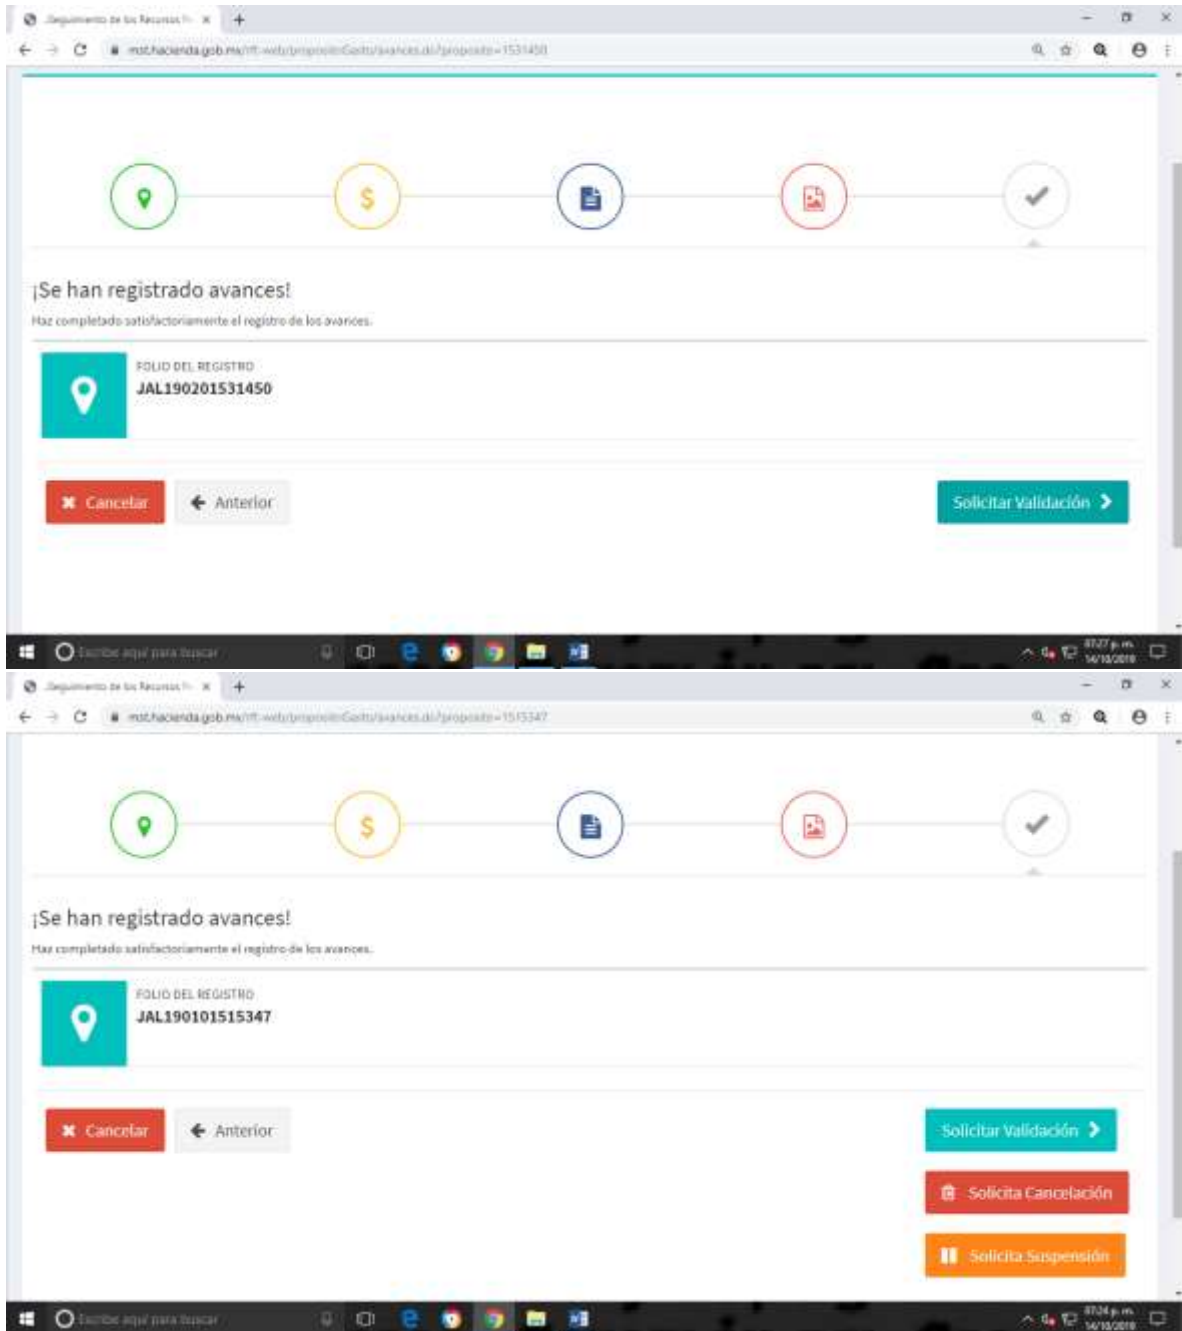

Supervision de obra

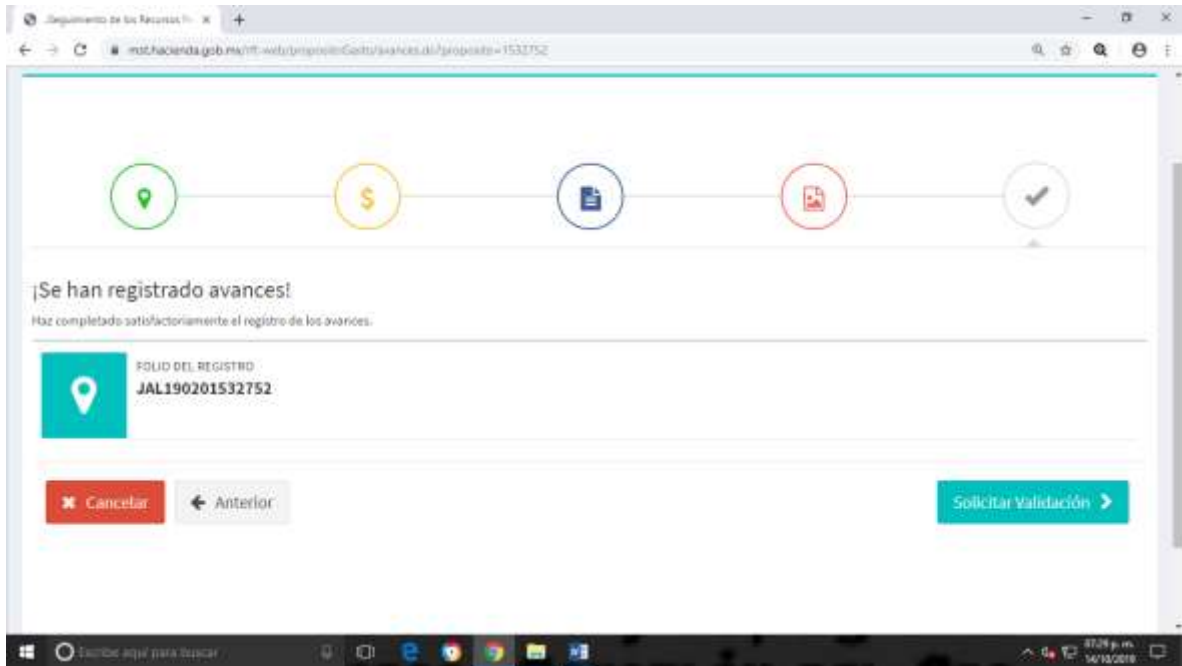

La taberna.

